# CPE 334 — Project Deliverable 1

Engineering baseline + working Sprint 1 · Theme 4 (E-Commerce / Ordering) · Campus Café Pre-order

| | |
|---|---|
| **Team** | vieng (GitHub `vienggg`) — **full name, student ID**<br>ninja (GitHub `NinjoMUDA`) — **full name, student ID** |
| **Repository** | github.com/vienggg/Food-order (public) |
| **Submitted version** | Branch `sprint-1`, commit `fe317d4`. Release on `main` / tag: **filled in when vieng merges the release** |
| **Project board** | github.com/users/vienggg/projects/4 (Backlog → Specified → Started → PR Review → Fixing → Done) |
| **Test result** | Server unit + API 63/63, client unit 5/5, end-to-end 20/20 (phone 375 px + desktop 1280 px), build OK; 46/46 acceptance criteria Pass — test-run.md, ac-results.md |

## 1. Evidence index

All documents live in the repository; links point to branch `sprint-1`. This PDF is an index, not a copy.

| Rubric part (points) | Artifact / link | IDs / what to look at | Status |
|---|---|---|---|
| A. SRS and product scope (10) | docs/srs.md | Actors §2; scope + exclusions §3; FR-01..FR-18 §4; BR-01..BR-07 §5; NFR-01..NFR-09 with measurable targets §6; assumptions AS-01..06, decisions DEC-01..08, questions Q-01..06 §7–9 | Merged (PR #19), reviewed |
| B. Feature inventory and traceability (10) | docs/features.md, docs/traceability.md | F-01..F-12 with sprint and requirements; every FR/BR/NFR → feature → sprint → AC → test → result; coverage check §4 | Merged (PR #17, #29); F-01..F-04 Verified |
| C. System-level SDS (15) | docs/system-sds.md | Architecture + where each rule is enforced §1; UI §2; data model §3; API conventions + shared JSON §4; role/permission matrix §5.2; sessions §6; configuration + GCP plan §7 | Merged (PR #20, #21) |
| D. Three-sprint plan (5) | docs/sprints/plan.md | Goals and dates per sprint; F-01..F-12 allocation; dependencies; Sprint 1 feasibility; remaining work; risks | Merged (PR #16) |
| E. Sprint 1 contracts (20) | docs/sprints/sprint-1/ | F-01-auth, F-02-menu, F-03-orders, F-04-accept: feature SDS, UI, API, data, AC (46), test spec (58 test IDs), DoD link, version history. Shared definition-of-done.md. Committed before code: see §3 | Merged with each feature PR |
| F. Working Sprint 1 and verification (20) | docs/evidence/ | test-run.md (every test, tested commit), ac-results.md (46/46), history.md (contract → red → green, PR/review table), `tdd/` red + green outputs, screenshots; §2–§4 below | All Pass |

## 2. Run it and test it

Needs Node 24 and Docker Desktop. Full steps: README.md.

```
npm install
cp server/.env.example server/.env      # set your own SEED_PASSWORD (never committed)
npm run db:up && npm run db:migrate && npm run db:seed
npm run dev                              # app http://localhost:5173, API :3000
npm test                                 # server 63 + client 5
npx playwright install chromium && npm run test:e2e   # 20 end-to-end (phone + desktop)
npm run evidence                         # re-runs everything and rewrites docs/evidence/*.md for the
current commit
```

Seeded accounts: `alice@cafe.test`, `bob@cafe.test` (CUSTOMER), `staff@cafe.test` (OPERATOR); password = your `SEED_PASSWORD`.

### Demo sequence (about 3 minutes)

| # | Step | Shows |
|---|---|---|
| 1 | Log in as alice with a wrong password → "Incorrect email or password."; then the right password → `/menu` | F-01, FR-01, DEC-02 |
| 2 | Croissant is greyed "Sold out" with a disabled +. Add Latte twice and Thai Milk Tea → one Latte line ×2, estimated ฿180.00 | F-02, BR-03, BR-02 (+1 on same line) |
| 3 | Place order → `/orders/N` "Order #N placed!", total ฿180.00 from the server, status PLACED | F-03, BR-04, BR-05 |
| 4 | Rejected case: in another tab mark an item sold out (or run TEST-F03-20); Place order → "Order not placed. 'Latte' is no longer available.", cart kept, nothing saved | BR-03, NFR-04 |
| 5 | Access case: as alice open `/operator/orders` → back to `/menu` "You don't have access to that page."; API answers 403 | FR-04, role matrix |
| 6 | Log out, log in as staff → queue oldest first → Accept → "Order #N accepted."; alice's order now ACCEPTED | F-04, FR-09, FR-10 |
| 7 | Race: TEST-F04-07 sends 20 accepts at once → exactly one 200 (run `npm test`) | BR-07 |

## 3. Engineering process evidence

### Contract → failing test → code (from history.md)

| Feature (owner) | Contract | Tests fail [red] | Code passes [green] | Pull request (reviewer) |
|---|---|---|---|---|
| F-01 Login (vieng) | `e187cf8` | `d0d4eb9` 11 failed | `eebaf41` 11 passed | #22 (ninja) |
| F-02 Menu (ninja) | `6e25979` | `3376cd3` 6 failed | `2816f63` 6 passed | #23 (vieng) |
| F-03 Orders (ninja) | `3178514` | `e922626` 29 failed | `13a2651` 29 passed | #26 (vieng) |
| F-04 Accept (vieng) | `92470d8` | `463f459` 10 failed | `f729818` 10 passed | #24 (ninja) |

Workflow: Issue on the board → branch from the Issue (`gh issue develop`) → PR into `sprint-1` → the other student reviews with a written check, approves and merges (merge commit, never squash); the author replies to each review. Examples of review findings that changed code: setup tests needed `prisma generate` (#18 → `bd502d0`); Vite cache committed on the F-04 branch (removed before #24); comment style on #26.

### Contribution

| Area | vieng | ninja |
|---|---|---|
| Requirements and design | SRS (Doc A); SDS §1, 2, 5, 6, 7 (architecture, UI, roles, auth, config) | Feature inventory + traceability (Doc B); SDS §3, 4 (data model, API); sprint plan (Doc D) |
| Features (contract, tests, code) | Setup skeleton (#1), F-01 login, F-04 accept | F-02 menu, F-03 orders, client test setup |
| Testing | Playwright setup, E2E for F-01, F-02, F-04; evidence script | E2E for F-03; traceability results; cross-review runs of every vieng PR |
| Reviews | Reviewed and merged #16, #17, #21, #23, #26, #27, #29 | Reviewed and merged #18, #19, #20, #22, #24, #25, #30 |


### AI-use declaration

Both students used Claude Code (Anthropic) as a coding and documentation assistant, each in their own session, working on bounded GitHub Issues with the feature contract as input. Tasks assisted: drafting documents (SRS, SDS, plan, contracts, traceability), writing failing tests first and then implementation, UI screens, running tests, opening PRs and drafting review comments. The two AI sessions coordinated through a private chat relay; each student's AI reviewed the other student's PRs by running the code and tests. Both students are responsible for the result and can explain every part; decisions were recorded in Issues, PR reviews and the documents above.


## 4. Known limitations and open items

- During setup (6 Nov, 02:18–02:48, documents only): PRs #13 and #15 were merged by their author without review, and four commits were pushed directly (`5f85976`, `810c7e3`, `2797462`, `d92baf0`). Every PR from #16 on was reviewed and merged by the other student. Details: history.md "Known exceptions".
- Branch `feature/F-03-e2e` is linked to Issue #10 through PR #27; the branch link under "Development" is added on the website.
- F-03 reads menu items without a row lock inside the order transaction; in Sprint 1 nothing changes availability at runtime, so no race exists yet. Revisit with F-05 (menu management).
- UI debt: desktop operator queue uses cards instead of a table; desktop My orders and Order detail are two pages instead of side by side.
- Release to `main`, tag `v0.1.0-sprint1` and GCP deployment are not done yet (deployment is Lab 5).


## 5. Screenshots (from the end-to-end run)





F-01 wrong password (phone)





F-02 menu, Croissant sold out





F-03 cart, Latte ×2, ฿180.00





F-03 order placed, server total





F-03 rejected: item sold out (BR-03)



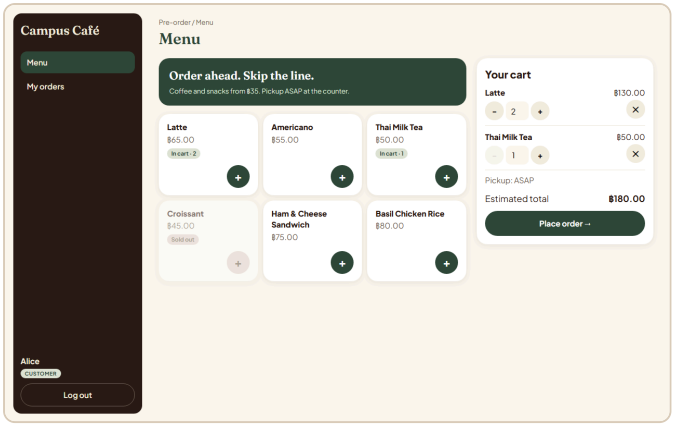

F-01 customer on operator page → own home



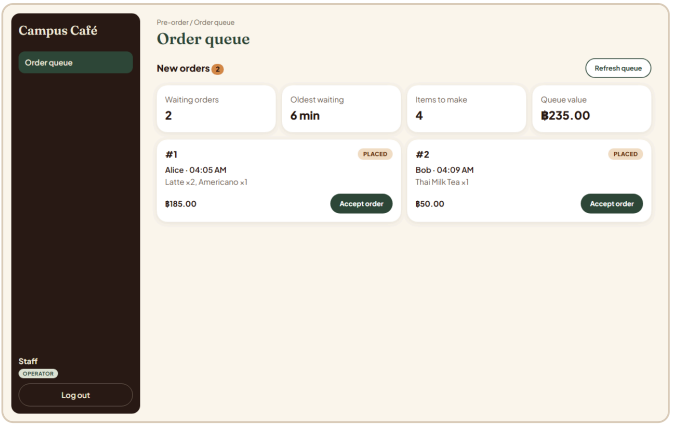

F-04 operator queue




F-04 already accepted (BR-07, 409)




F-03 menu + cart (desktop 1280 px)




F-04 queue (desktop 1280 px)
